Oregon Department of Transportation 000T Regin 2 | 455 Aiport Rd., Bldg B | Salem, OR 97301

Project Update

The project is proceeding ahead of schedule, with westbound ramps estimated to open in mid-to-late May. The contractor, K&E Excavating, Inc., and its subcontractors have worked diligently to minimize the disruption to the community and complete the current stage of the project sooner than estimated.

Drivers should look for roadside signs with more information about upcoming traffic changes, including the switch to the westbound section of the highway.

A new temporary connection for the eastbound off-ramp will also be open. Crews will begin replacing eastbound bridges and will widen Cascade Highway

beneath the overpass. Please note that shortly after traffic is switched, Cascade Highway will be closed for one to two days for eastbound bridge demolition. Follow signs to detour routes. Eastbound traffic should use the on-ramps at Fernridge Road or Golf Club Road while contractors work on the new eastbound ramps.

A diagram is included on the other side of this flyer, and all of this information is available on the project Web site, www. sublimityinterchange.com. You can also sign up to receive ODOT's news releases via email, including weekly construction updates.

Please contact us with any questions, concerns or comments about the project.


Contacts:

Shane Ottosen, Project Manager shane.ottosen@odot.state.or.us (503) 986-2698
Ray Bryant, Asst. Project Manager raymond.g.bryant@odot.state.or.us (503) 986-2684

Scouts from Pack 50 visit the project site on April 24



www.sublimityinterchange.com

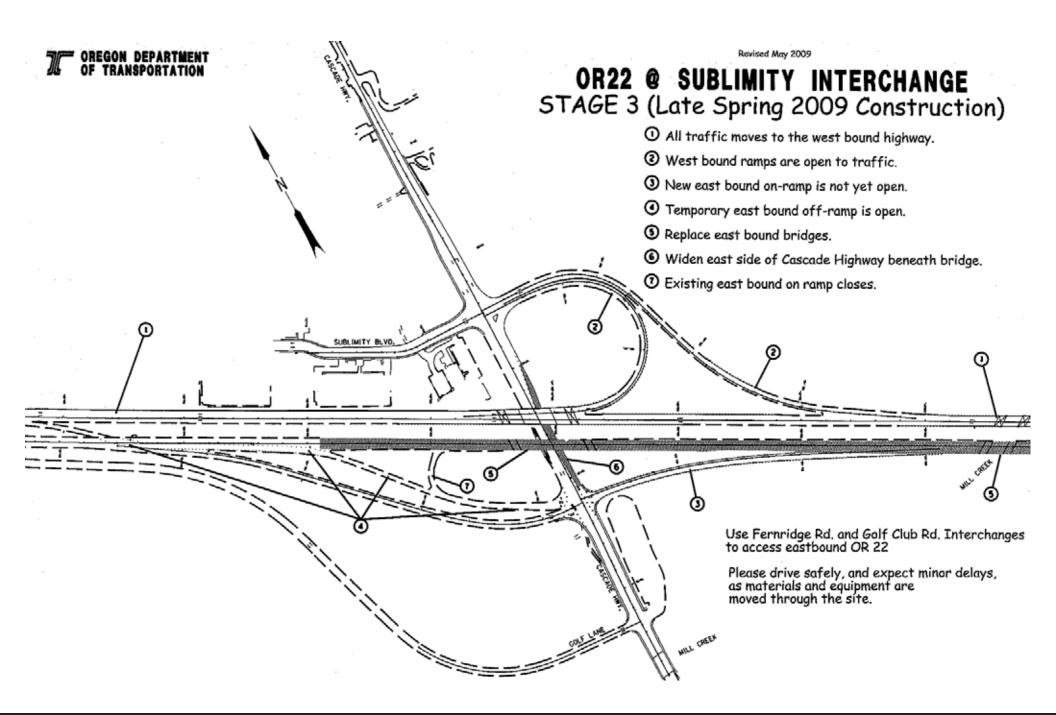

www.sublimityinterchange.com
